



NEXUSNTU

CHANGE MANAGEMENT PLAN

Version 1.0
10/21/2025

VERSION HISTORY

Version #	Implemented By	Revision Date	Approved By	Approval Date	Reason
1.0	Akshay Krishna	10/21/2025	Aishwarya Anand	10/28/2025	Initial Change Management Plan

UP Template Version: 11/30/06

TABLE OF CONTENTS

1 INTRODUCTION	5
1.1 Purpose of The Change Management Plan	5
2 CHANGE MANAGEMENT PROCESS	5
2.1 Change Request Process Flow Requirements	5
2.2 Change Request Form and Change Management Log	6
2.3 Evaluating and Authorizing Change Requests	6
2.3.1 Change Control Board	7
3 RESPONSIBILITIES	7
APPENDIX A: CHANGE MANAGEMENT PLAN APPROVAL	8
APPENDIX B: REFERENCES	9
APPENDIX C: KEY TERMS	10
APPENDIX D: CHANGE REQUEST FORM EXAMPLE	11
APPENDIX E: CHANGE MANAGEMENT LOG TEMPLATE	12

1 INTRODUCTION

1.1 PURPOSE OF THE CHANGE MANAGEMENT PLAN

The Change Management Plan for the NEXUSNTU project provides a structured framework for managing all project changes from inception through delivery. This plan ensures that all change requests are properly documented, evaluated, and processed in a consistent and transparent manner.

This document establishes the procedures, roles, and responsibilities required to effectively manage changes to project scope, schedule, budget, resources, and deliverables. It serves as the authoritative guide for all stakeholders involved in the change management process.

Purpose

- Document and track all changes to project baselines
- Establish clear procedures for submitting and processing change requests
- Define roles and responsibilities for change management
- Ensure proper evaluation and authorization of changes
- Maintain project integrity while accommodating necessary modifications

Intended Audience:

- Project Manager
- Project Team Members
- Project Sponsor
- Change Control Board Members
- Senior Leadership
- Project Stakeholders


2 CHANGE MANAGEMENT PROCESS

The Change Management process establishes an orderly and effective procedure for tracking the submission, coordination, review, evaluation, categorization, and approval for release of all changes to the project's baselines.

2.1 CHANGE REQUEST PROCESS FLOW REQUIREMENTS

The NEXUSNTU project follows a five-step change request process to ensure all changes are properly managed:

Step	Description
Generate CR	A submitter identifies a need for change and completes a Change Request (CR) Form. The completed form is submitted to the Change Manager via email or the project management system.
Log CR Status	The Change Manager assigns a unique CR number and enters the CR into the Change Management Log within 24 hours of receipt. The CR's status is updated throughout the process.
Evaluate CR	The Project Manager, in consultation with relevant team members and subject matter experts, reviews the CR to assess: impact on scope, schedule, and budget; technical feasibility; resource requirements; risks and dependencies; and proposed solution. A detailed impact analysis is documented within 3-5 business days.
Authorize	The Change Control Board (CCB) reviews the evaluation and impact analysis. The CCB meets weekly or on an ad-hoc basis for urgent requests. The board approves, rejects, or requests additional information for each CR. Authorization decisions are documented with rationale.
Implement	If approved, the Change Manager coordinates with the project team to implement the change according to the approved plan. Updates are made to relevant project documents (scope, schedule, budget, etc.). The submitter and stakeholders are notified of the CR status and implementation timeline. Upon completion, the CR is closed and lessons learned are documented.

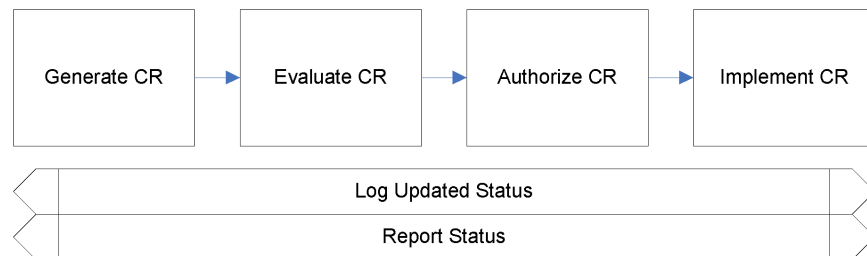

2.2 CHANGE REQUEST FORM AND CHANGE MANAGEMENT LOG

All change requests must include the following data elements to ensure proper tracking and evaluation:

Element	Description
Date	The date the CR was created
CR#	Unique identifier assigned by the Change Manager
Title	A brief description of the change request
Description	Description of the desired change, the impact, or benefits of a change should also be described
Submitter	Name of the person completing the CR Form and who can answer questions regarding the suggested change
Phone	Phone number of the submitter
E-Mail	Email of the submitter
Product	The product that the suggested change is for
Version	The product version that the suggested change is for
Priority	A code that provides a recommended categorization of the urgency of the requested change (High, Medium, Low)
Type	Category of change
Impact Analysis	Assessment of effects on project constraints
Estimated Effort	Time and resources required to implement the change
Status	Current state of the CR in the process flow
Assigned to	Team member(s) responsible for evaluation or implementation
Target Date	Expected completion date for the change
Actual Completion	Date when the change was fully implemented
CCB Decision	Approved, Rejected, or Deferred with rationale

The Change Management Log is maintained by the Change Manager and is accessible to all project stakeholders through the project repository. The log is updated in real-time and reviewed during weekly project status meetings.

2.3 EVALUATING AND AUTHORIZING CHANGE REQUESTS

Change requests are evaluated using the following priority criteria:

Priority	Description
High	Changes that are critical to project success, address significant risks, prevent project failure, resolve blocking issues affecting multiple stakeholders, or are required by regulatory/compliance mandates. Must be addressed immediately.
Medium	Changes that improve project outcomes, enhance functionality, address moderate risks, or optimize resource utilization. Should be addressed within normal workflow. Examples: feature enhancements, process improvements, moderate bug fixes
Low	Changes that provide minor improvements, cosmetic updates, or nice-to-have features. Can be scheduled based on resource availability. Examples: UI refinements, documentation updates, minor usability improvements.

Change requests are evaluated and assigned one or more of the following change types:

Type	Description
Scope	Changes affecting project scope, objectives, deliverables content, or acceptance criteria. Requires formal baseline update.
Time	Changes affecting project timeline, milestones, phase durations, or deadline commitments. Requires schedule baseline update.
Duration	Changes affecting the duration of specific tasks or activities without impacting overall project timeline.
Cost	Changes affecting project budget, funding allocation, resource costs, or financial commitments. Requires budget baseline update.
Resources	Changes affecting team composition, resource allocation, skill requirements, or external vendor engagement.
Deliverables	Changes affecting the characteristics, specifications, quality attributes, or acceptance criteria of project outputs.
Product	Changes affecting product features, functionality, architecture, technology stack, or user experience design.
Processes	Changes affecting project methodologies, workflows, procedures, governance structures, or communication protocols.
Quality	Changes affecting quality standards, testing requirements, acceptance criteria, or compliance requirements.
Risk	Changes introduced to mitigate identified risks or address emerging risk factors.

Change requests are evaluated and assigned one of the following status types:

Status	Description
Open	Entered/Open but not yet approved or assigned
Work in Progress	CR approved, assigned, and work is progressing
In Review	CR work is completed and in final review prior to testing
Testing	CR work has been reviewed and is being tested
Closed	CR work is complete, has passed all tests, and updates have been released.

2.3.1 Change Control Board

The Change Control Board (CCB) is a formally constituted group of stakeholders responsible for reviewing, approving, or rejecting changes to the NEXUSNTU project baselines.

Role	Name	Contact	Description
Project Manager	Aishwarya Anand		Holds the final approval authority for all Change Requests (CRs) and acts as the default approver for any CRs not covered by other Change Control Board (CCB) members.
Change Manager	Akshay Krishna		Oversees all documentation and procedures related to quality assurance, risk management, and change control processes.
Lead Developer	Tran Son Viet	[Insert Contact #]	Authorizes all technical and software-related changes, including updates to both front-end and back-end systems such as architecture and user interface design.
Financial Controller	Vu Thao Nguyen		Oversees project finances and ensures that all approved Change Requests comply with the allocated budget.

3 RESPONSIBILITIES

Role	Name	Contact	Description
Project Manager	Aishwarya Anand		Reviews and approves Change Requests (CRs) within the designated timeframe according to their priority. Conducts the final assessment before release, ensures proper documentation backup, and uploads approved changes to the team's Wiki.
Change Manager	Akshay Krishna		Approves CRs based on priority and deadlines. Organizes Change Control Board (CCB) meetings when required. Keeps track of all CR records, assigns CR numbers, and maintains an up-to-date Change Request Log.
Lead Developer	Tran Son Viet		Reviews and authorizes CRs within the required timeframe. Oversees the technical execution of software modifications and reports progress regularly to the Change Manager.
Financial Controller	Vu Thao Nguyen		Conducts preliminary financial assessments of CRs and advises on approval decisions based on the projected financial implications.
Head of Communication	Nguyen Phuong Linh		Manages communication between project stakeholders and the development team. Ensures the change management process and newly implemented updates are clearly conveyed to all stakeholders.

Appendix A: Change Management Plan Approval

The undersigned acknowledge they have reviewed the NexusNTU **Change Management Plan** and agree with the approach it presents. Changes to this **Change Management Plan** will be coordinated with and approved by the undersigned or their designated representatives.

Print Name: Aishwarya Anand Date: 10/28/2025

Title: Miss

Role: Project Manager

Print Name: Akshay Krishna Date: 10/28/2025

Title: Mr.

Role: Change Manager

Print Name: Vu Thao Nguyen Date: 10/28/2025

Title: Miss

Role: Financial Controller

Print Name: Tran Son Viet Date: 10/28/2025

Title: Mr.

Role: Lead Developer

Print Name: Nguyen Phuong Linh Date: 10/28/2025

Title: Miss

Role: Head of Communications

Appendix B: References

The following table summarizes the documents referenced in this document.

Document Name and Version	Description	Location
CDC_UP_Change_Management_Plan_Template	Initial Template	NTULEARN
LarkDetect_Change_Management_Plan_v1.0	LarkDetect Change Management Plan	NTULEARN

Appendix C: Key Terms

The following table provides definitions for terms relevant to this document.

Term	Definition
Change Request (CR)	A formal proposal to modify any aspect of the project, including scope, schedule, budget, deliverables, or resources.
Change Control Board (CCB)	A governing body of project stakeholders responsible for reviewing, evaluating, and approving or rejecting change requests.
Change Manager	The individual responsible for tracking, documenting, and coordinating all change requests throughout their lifecycle.
Baseline	The approved version of a project plan, scope, schedule, or budget that serves as a reference for measuring progress and performance.
Impact Analysis	The process of assessing the potential effects of a proposed change on project scope, timeline, cost, resources, and risks.
Priority Level	The classification of a change request based on urgency and potential impact (High, Medium, or Low).
Change Management Log	A centralized record that tracks the status, approval history, and implementation progress of all submitted change requests.
Stakeholder	Any individual or group with an interest in the project outcome or who may be affected by project changes.
Implementation Plan	A documented strategy outlining how an approved change will be executed, monitored, and verified for completion.
Scope Change	A modification to the project's agreed deliverables, boundaries, or objectives that may affect other project baselines.
Change Request (CR)	A formal proposal to modify any aspect of the project, including scope, schedule, budget, deliverables, or resources.
Change Control Board (CCB)	A governing body of project stakeholders responsible for reviewing, evaluating, and approving or rejecting change requests.
Change Manager	The individual responsible for tracking, documenting, and coordinating all change requests throughout their lifecycle.
Baseline	The approved version of a project plan, scope, schedule, or budget that serves as a reference for measuring progress and performance.

Appendix D: Change Request Form Example

The example Change Request Form attached below can be used to submit changes during the life of the project.



CDC_UP_Change_Request_Form_Example

Appendix E: Change Management Log Template

The detailed Change Management Log template attached below can be used to track and manage requested changes during the life of the project.



CDC_UP_Change_M
anagement_Log_Terr
